


ID	Task Name	Start	Finish	Duration	Jul 2011		Aug 2011					Sep 2011				Oct 2011				Nov 2011			
					7/24	7/31	8/7	8/14	8/21	8/28	9/4	9/11	9/18	9/25	10/2	10/9	10/16	10/23	10/30	11/6	11/13	11/20	
1	PDB Cables	7/22/2011	7/29/2011	1.2w																			
2	Prepare Delivery of PDB components to 3W	7/22/2011	7/29/2011	1.2w																			
3	Complete New PDB Assembly Instructions	7/28/2011	7/29/2011	.4w																			
4	3W assembles first 2 PDB units	8/2/2011	8/12/2011	1.8w																			
5	Test first 2 PDB units	8/15/2011	8/19/2011	1w																			
6	3W assembles remaining 196 PDBs	8/22/2011	10/10/2011	7.2w																			
7	Test PDBs	9/12/2011	12/9/2011	13w																			
8	LV Power Supply Test Setup	7/22/2011	8/12/2011	3.2w																			
9	HV Power Supply Test Setup	7/22/2011	8/19/2011	4.2w																			
10	Test LV Power Supplies	8/15/2011	10/28/2011	11w																			
11	Test HV Power Supplies	8/22/2011	9/30/2011	6w																			
12	Determine Cable Lengths and Layout	8/29/2011	9/16/2011	3w																			
13	ECLinc/Unlimited Services Make Cables	9/12/2011	10/28/2011	7w																			
14	Specify and Order Relay Racks	8/1/2011	8/12/2011	2w																			
15	Test Relay Rack Configuration and Temp.	9/19/2011	10/7/2011	3w																			
16	Prepare Shipment of PS to FD	10/31/2011	11/4/2011	1w																			

**NOvA Project
Schedule**

July – November 2011

Rev 1.2

9/16/11

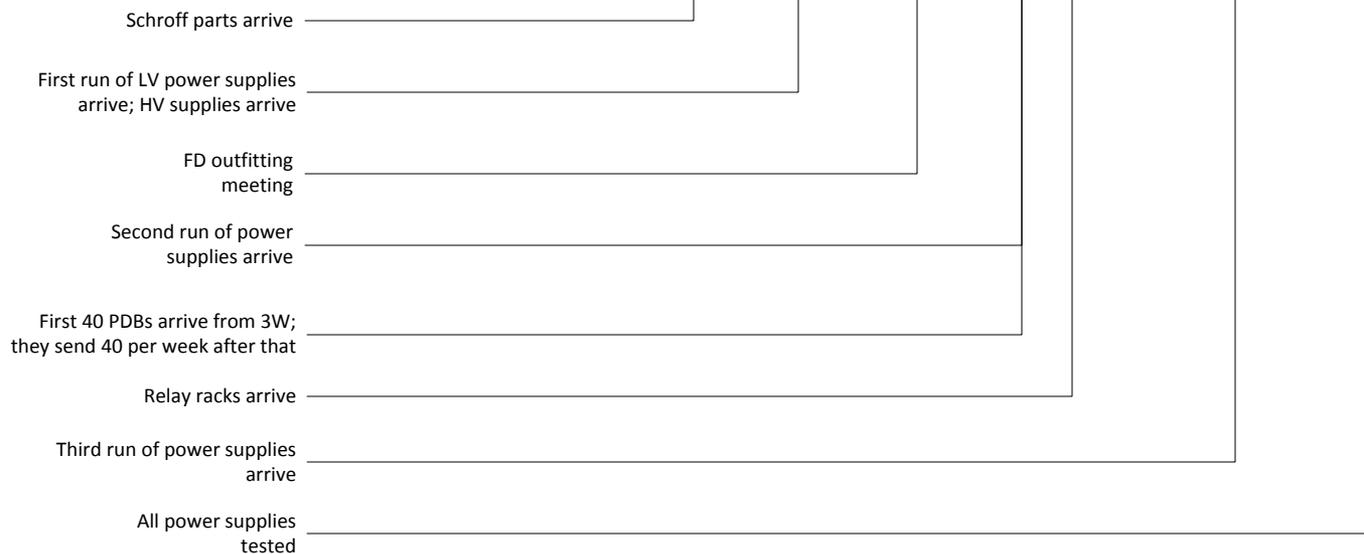

- = Completed
- = In Process
- = Not Started
- = On Hold
